


**TRANSPORTATION &
CAPITAL IMPROVEMENTS
(TCI)**

**INGRAM RD:
(CULEBRA TO MABE)
MARCH 31, 2015**


2012 Bond Project

**Presenter: Peter Rodriguez
Capital Projects Officer
Location: Carlos Coon Elementary
3110 Timber View Dr.**



Agenda

- **TCI Mission**
- **TCI Introductions**
- **Ingram Rd Project**
 - **Planned improvements**
 - **Traffic Control/Sequence of Work**
 - **Traffic Detours**
 - **Schedule**
- **Public Comments and Questions**



TCI Mission & Core Values

- **January 2014**


Public Works and CIMS consolidated to become Transportation and Capital Improvements (TCI)

- **TCI Mission**

Through innovation and dedication, we build and maintain San Antonio's infrastructure.


- **TCI & City's Core Values**

- ✓ Integrity: We model ethical behavior.
- ✓ Teamwork: We work together to make San Antonio better
- ✓ Innovation: We are driven by continuous improvement
- ✓ Professionalism: We are qualified, skilled and competent



Introductions

- **City Council District 6**
Office of Councilman Ray Lopez
- **TCI Construction Team**
David Pulido P.E. – Project Manager
Lisa Torres – Senior Engineering Associate
Peter Rodriguez – Capital Projects Officer
John De La Rosa – Inspections Supervisor
Marta Luitin-Atkin - Inspector
- **Contractor – Capital Excavation Company**
Layne Walker – Project Coordinator
Troy Wanner – Superintendent




Ingram Road (Culebra to Mabe/Potranco)







Planned Improvements

- \$7.8M allocated from the 2012 GO Bond Program
- Ingram to be reconstructed with 4-11' lanes, including 5' bike lanes, sidewalks (4 – 6 ft), driveways, and curbs
- Drainage Improvements include Storm Drains and Culvert
- Traffic signal upgrades at Culebra & Mabe/Potranco
- SAWS Water & Sanitary Sewer replacement
- Six (6) foot sidewalks on both sides of Mabe Road from Ingram to Joe Newton




Planned Improvements

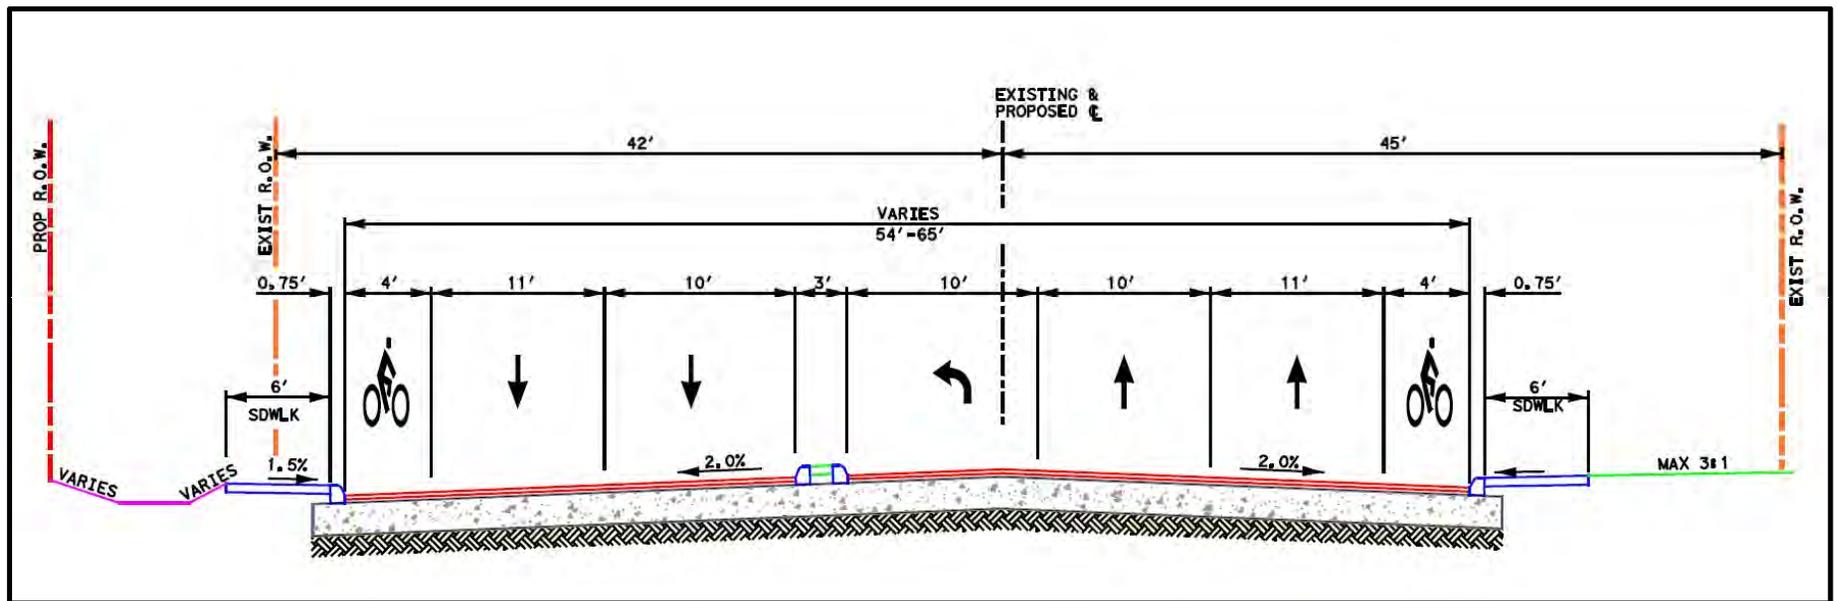



Traffic Control Plan/Sequence of Work


- Two-way traffic along Ingram maintained during all phases of construction
- Six (6) day work week for construction – sunup to sundown
- Traffic detours with signing (Mabe & Potranco closures); message boards will be used
- Preparing for construction: TCI will notify all affected services (VIA,EMS, USPS, etc), Council Office, residents, etc.
- TCI will provide updates via website/eblast; please check box in sign-in sheet for inclusion



Traffic Control Plan/Sequence of Work

Sequence of Work (all durations are weather permitting)


- Phase 1A – Temporary Pavement and SS Crossing - duration approx. 3.5 weeks
 - Sanitary Sewer Work (completed)
 - Temporary widening on the North side of Ingram Road (underway)
- Phase 1 – Construct South Side of Ingram - duration approx. 14 weeks
 - Move traffic to north side of Ingram
 - Construct SAWS water and sanitary sewer
 - Construct roadway, storm drains, and culvert
 - Construct curbs, sidewalks and driveways
- Phase 2: Construct the North side of Ingram – duration approx. 14 weeks
 - Move traffic to the south side of Ingram
 - Install signals at Culebra/Ingram
 - Construct roadway, storm drain, and culvert
 - Construct curbs, sidewalks and driveways



Traffic Control Plan/Sequence of Work

Sequence of Work (all durations are weather permitting)


- Phase 3 -Construct Mabe Road (Ingram to Joe Newton) – duration approx 8 weeks
 - Mabe to be closed; detour posted
 - Install signals at Mabe/Ingram intersection
 - Construct raised median on (Ingram, near Culebra)
 - Construct roadway, curbs, sidewalk, driveways
 - Mill & Overlay
- Phase 4 - Construct Potranco Rd - duration approx. 8 weeks
 - Potranco to be closed; detour posted
 - Construct roadway, curbs, sidewalk, driveways & remaining utility work
 - Install signals at Ingram/Potranco intersection
 - Construct raised median along Potranco




Traffic Control Plan/Sequence of Work


Sequence of Work (all durations are weather permitting)

- Phase 4B – Construct Raised Median & Mill – duration approx 1.5 weeks
 - Construct remainder of raised median
 - Mill (Ingram)
- Phase 5 – Signals, Final Mat & Overlay – duration approx. 10 weeks
 - Complete traffic signals at Mabe/Potranco intersection
 - Landscaping
 - Install Permanent pavement markings





Traffic Detours

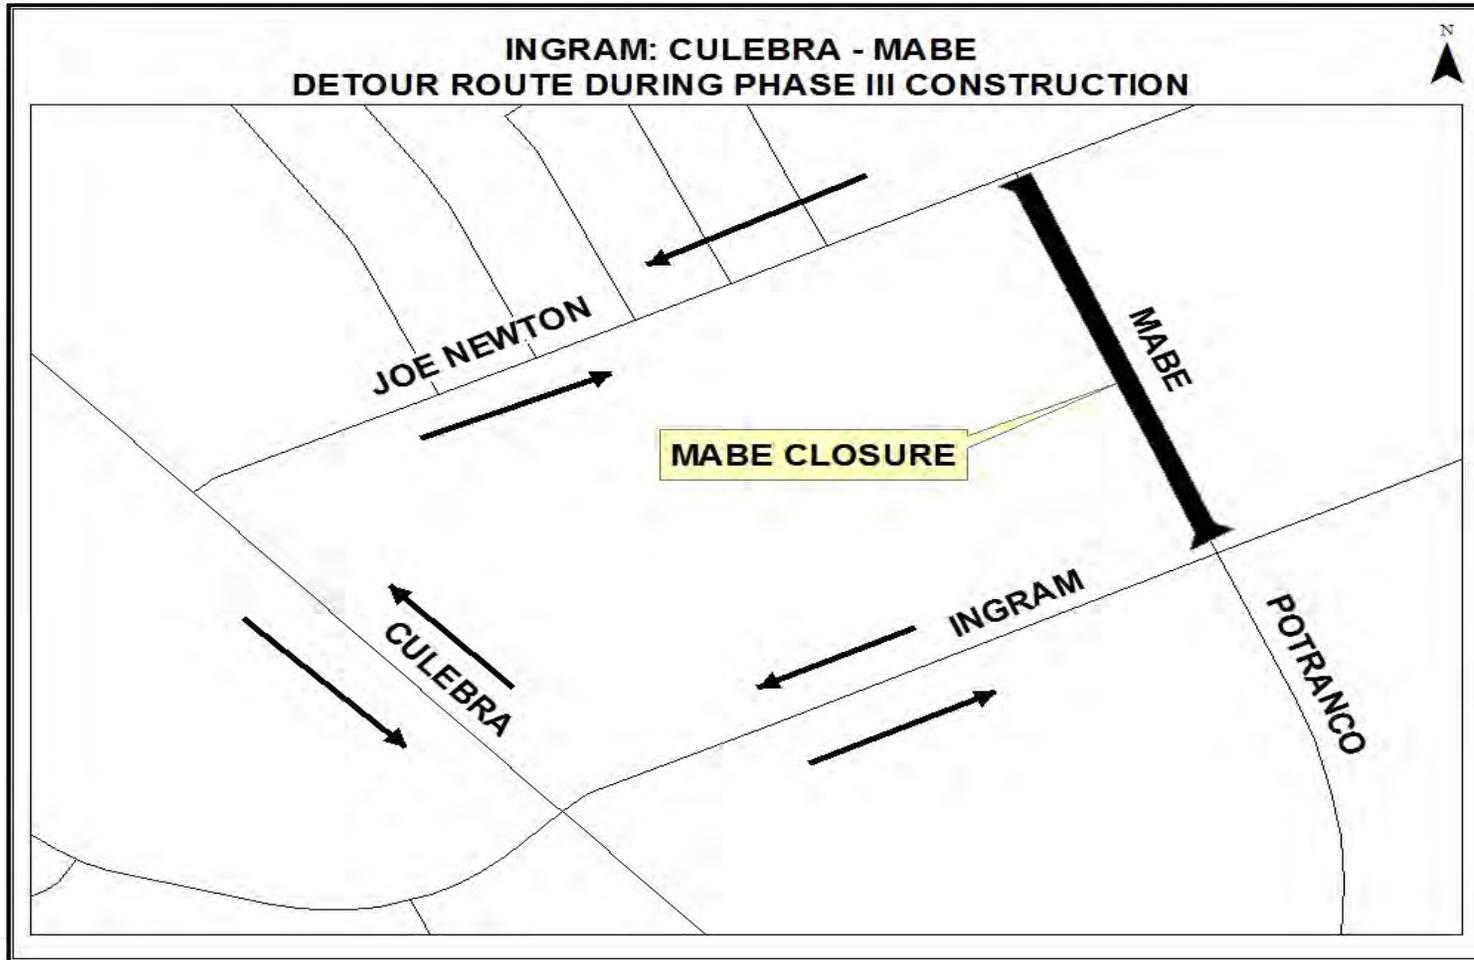



Traffic Detours

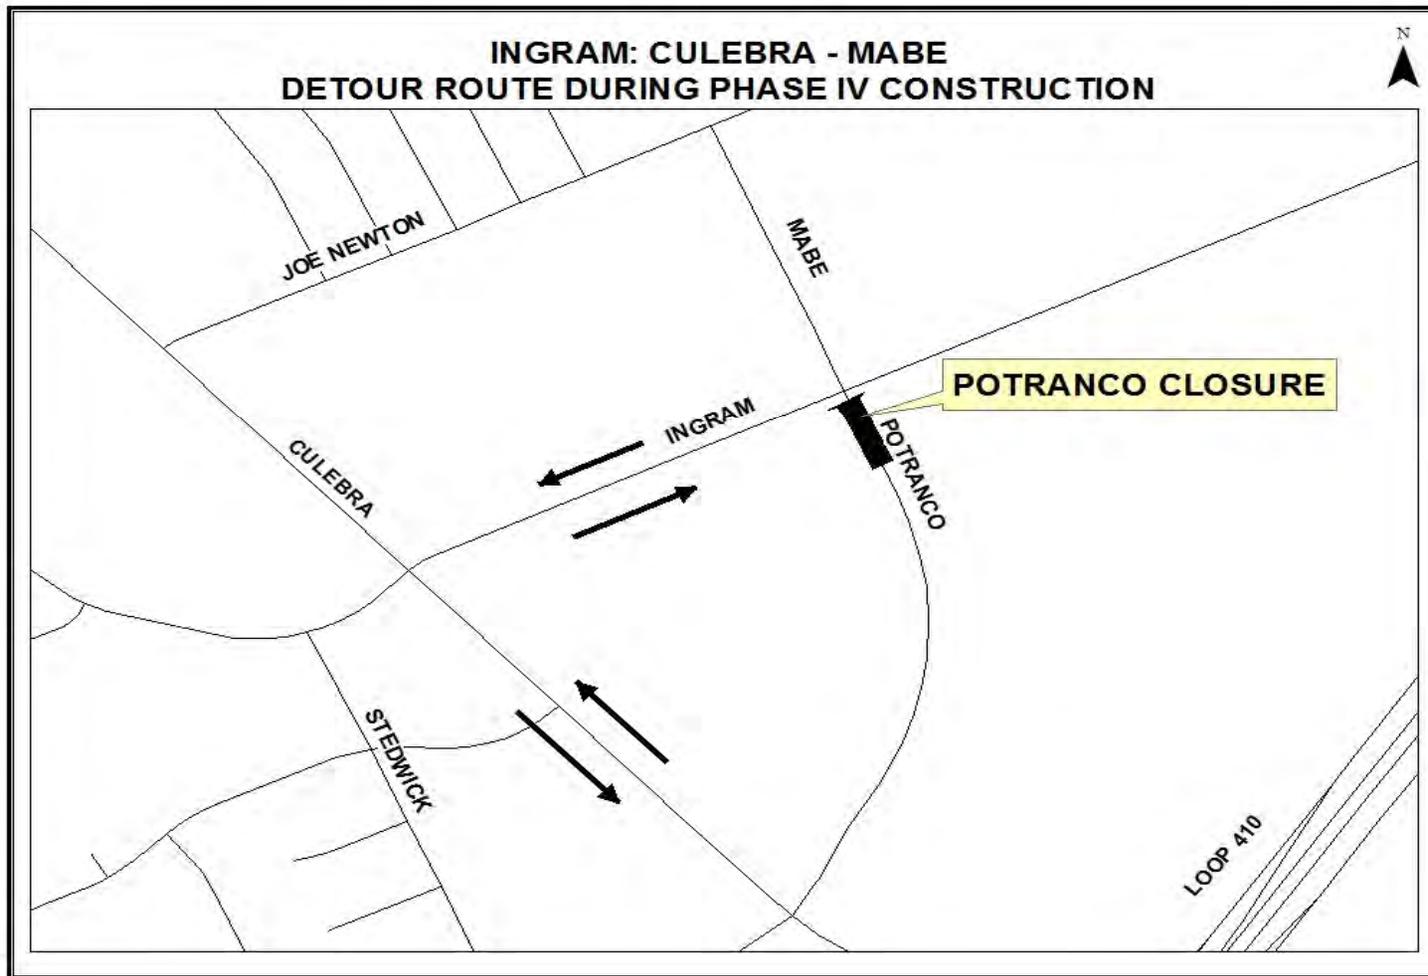




Project Schedule

Ingram Road Schedule	
Construction start	March 16, 2015
Estimated construction completion*	May 2016
Estimated construction duration*	14 months
*Weather Permitting	

For information in regards to the project during the construction phase please contact:
Peter Rodriguez – Capital Projects Officer at 210.207.8154
or at pete.rodriquez@sanantonio.gov

If you would like to be added to an e-mail list for project updates or future meeting announcements, please ensure you fill out the sign-in sheet and check the permission block.



Questions or Comments



TCI Thanks You for Your Attendance
